


# I-95 EXPRESS LANES FREDERICKSBURG EXTENSION (FRED EX)


Project Update

 Marcie Parker, P.E.  
Fredericksburg District Engineer

December 4, 2018

# Fred Ex Project Scope

- Extends I-95 Express Lanes 10 miles south of Route 610 Garrisonville Road (Exit 143) to Route 17 (Exit 133)
- Direct connection to the I-95 Southbound (*under construction*) and Northbound (*future*) Rappahannock River Crossing projects
- New access points
  - Quantico / Russell Road in Prince William County
  - Courthouse Road in Stafford County
  - Route 17 in Stafford County

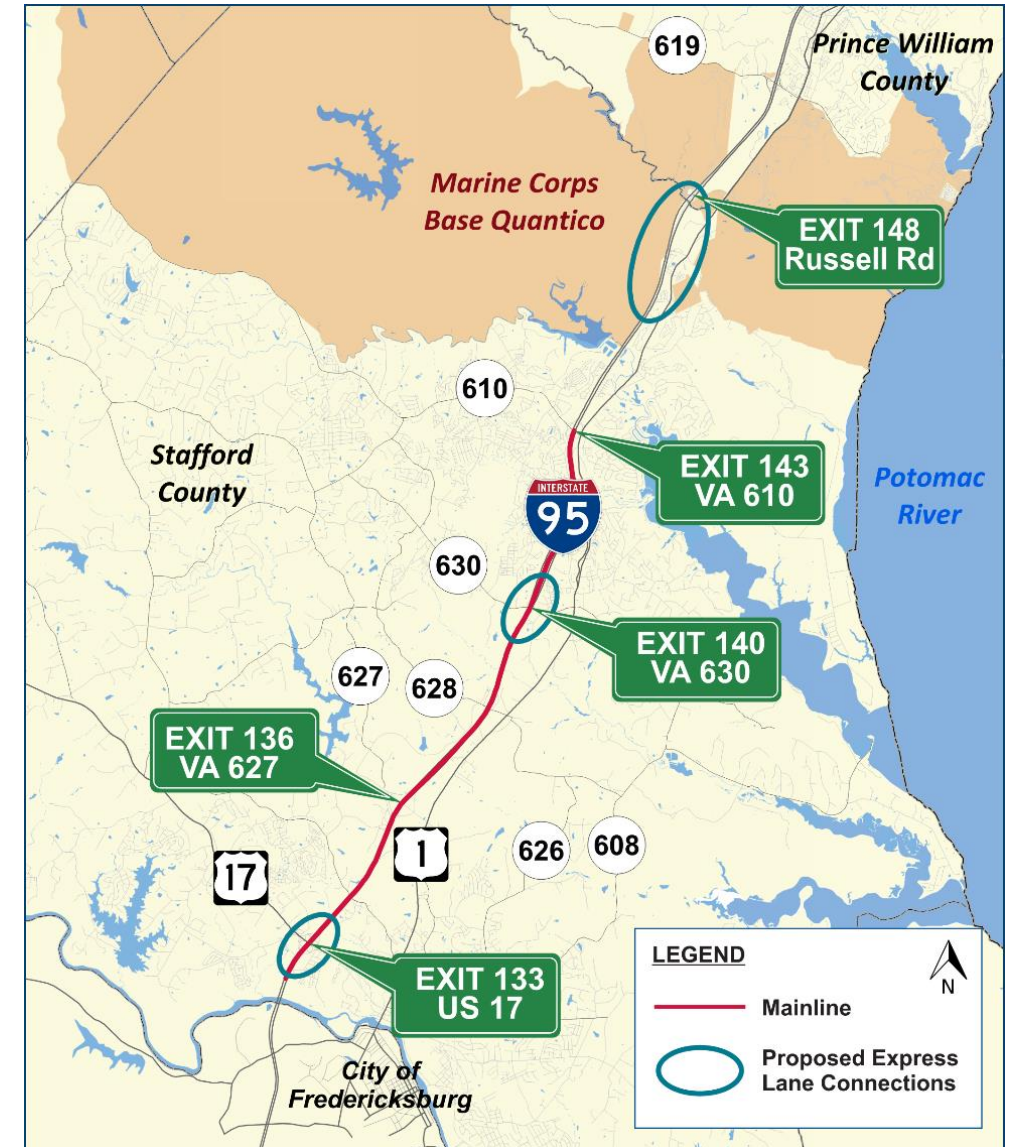

# Fred Ex Project Schedule

*VDOT / 95 Express Lanes LLC sign Advanced Development Framework Agreement*

*June 2017*

*Public Hearing*

*September 2017*

*95 Express Lanes LLC proposal for FredEx accepted*

*January 2018*

*Final NEPA Decision (FONSI) issued*

*March 2018*

*Design Build Procurement*

*Ongoing*

**Commercial Close**

**Winter 2019**

**Financial Close**

**Spring 2019**

**Begin Construction**

**Summer 2019**

**Service Commencement**

**Fall 2022**

# Action Items for January

## HOT/HOV Designation

- Designate the I-95 Express Lanes Fredericksburg Extension as HOT Lanes
- Specify the high-occupancy requirement for the I-95 Express Lanes Fredericksburg Extension as HOV-3
- Authorize the Commissioner of Highways to establish the conditions for use of the I-95 Express Lanes Fredericksburg Extension

## Tolling Memorandum Of Understanding Approval

- Approve and authorize the Commissioner to execute a Tolling MOU with FHWA/USDOT relating to tolling on I-95 Express Lanes Fredericksburg Extension.
